

# **MEASURE G ACTIVITY**

## **January – March 2017**

- \$236,126 expended this quarter
- Will spend out Measure G by June 30

# **MEASURE Q ACTIVITY**

## **January – March 2017**

### **Program Overview:**

- **\$12,374,885 expended this quarter**
  - **Board approved sale of Tranche 2 bonds in amount of \$90M**
  - **Submitted additional materials in support of State funding for Library Project**
  - **District Wayfinding Signage Standards**
  - **Development of Donor Recognition Signage Plan**
  - **Review of proposed revisions to District Standards**
- 

# HORTICULTURE PROJECT



- Construction substantially completed
- Ribbon Cutting Ceremony April 5

# PERFORMING ARTS BUILDING RENOVATION



- Construction 99% complete
- Completion target May 2017
- Move-back in progress
- Costume Shop in B1800
- Ribbon Cutting August 16
- Occupancy fall 2017

# BIOTECHNOLOGY AND SCIENCE BUILDING



- Construction 62% complete
- Cabinetry installation almost done
- Floor finishes starting
- Furniture and equipment orders nearly completed
- Completion for fall semester
- Ribbon Cutting September 6

# VACAVILLE CENTER INTERSECTION IMPROVEMENTS PROJECT



- Construction contract awarded in April
- Completion target September 15

# AUTOTECHNOLOGY BUILDING



- Construction 50% complete
- Exterior stucco in progress
- Interior gypboard in progress
- Completion for fall occupancy
- Ribbon Cutting September 20

# VALLEJO CENTER HVAC UPGRADE

- Construction contract awarded
- Construction summer 2017
- Summer school at Georgia Street facility and MIT




# SOFTBALL BLEACHER REPLACEMENT



- Construction contract awarded
- NTP pending DSA plan approval
- Target completion date  
September

# FAIRFIELD CAMPUS ENTRY SIDEWALK

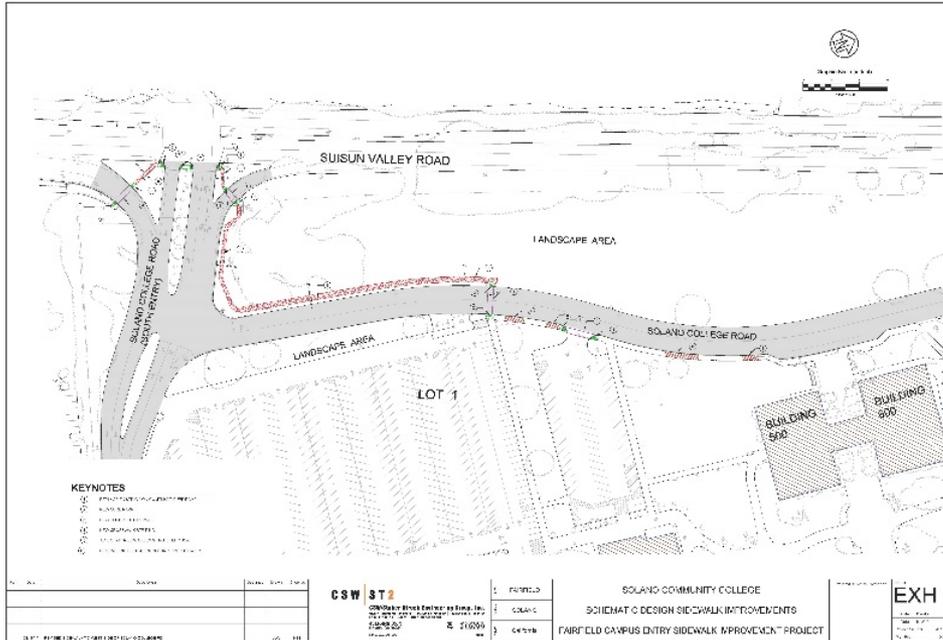

- Entry driveway to entry plaza at Administration Building
- Issue for bid in May
- Construction start July
- Solano County Transportation Authority approved \$50,000 funding contribution

# SCIENCE BUILDING - PHASE 1



- Development of construction documents in progress
- Sitework package submitted DSA
- Groundbreaking August 2



PROPOSED MAIN ENTRY SIGNAGE  
H&A

# VACAVILLE CLASSROOM BUILDING (ANNEX)



- Renovation design in progress
- Additional roof truss testing in May/June
- Construction start target November 2017

# QUESTIONS?

