

MEASURE Q ACTIVITY

OCTOBER – DECEMBER 2017

Program Overview:

- \$8,185,202 expended this quarter
- Completed project close out for:
 - Performing Arts Building Renovation
 - Vacaville Biotechnology & Science Building
 - Vallejo Autotechnology Building
 - Vallejo Center (HVAC Upgrade)
- Prepared District Standards Revisions
- Board appointed new CBOC members
 - CBOC working on FY 15-16 Annual Report



FAIRFIELD INFRASTRUCTURE PROJECTS



SUB-STATION REPLACEMENT

- Installation and Campus power shutdown over Winter Break
- Minor finishing work in progress

B-100 DATA CENTER GENERATOR

- Contract awarded
- Construction in May

GAS LINE REPLACEMENT

- In progress

SCIENCE BUILDING - PHASE 1






- Underground utilities completed
- New switchgear set
- Building pad developed
- Construction of foundation and underslab utilities in progress
- Occupancy January 2019



PROPOSED MAIN ENTRY SIGNAGE



LIBRARY/LEARNING RESOURCE CENTER

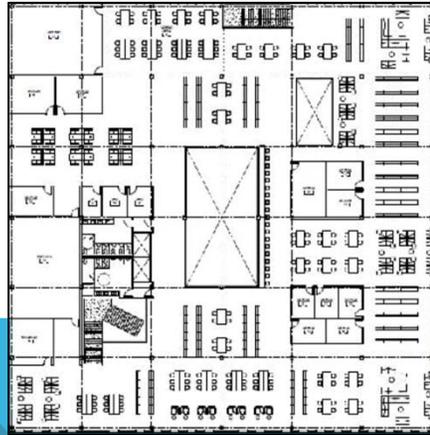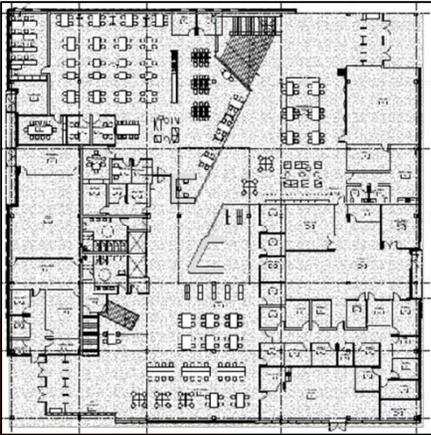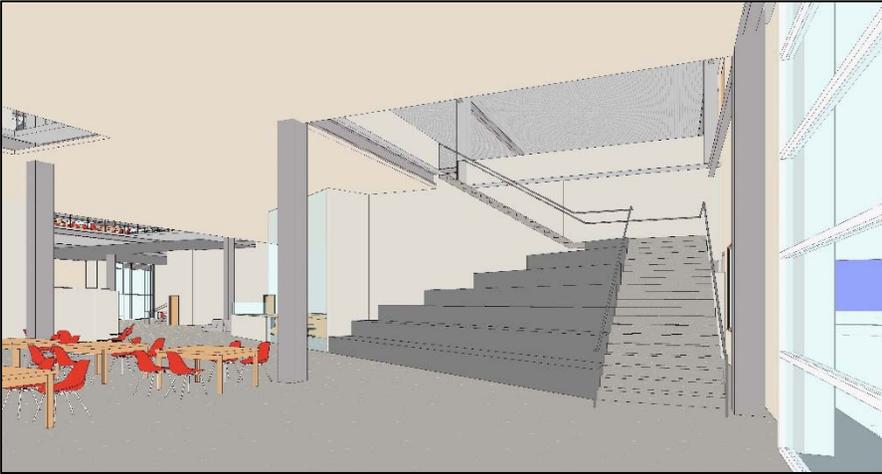

- Architect selected
- Visioning sessions conducted
- Schematic design in progress
- Site survey and geotechnical report completed
- CEQA Mitigated Neg Dec Report completed; currently in public review period

HORTICULTURE RESTROOM BUILDING



- Contract awarded for modular building
- Sitework bids received in January
- Completion target: May 2018



SOFTBALL BLEACHER REPLACEMENT



- Bleachers and press box completed
- Construction contract awarded for sidewalk to restroom building
- Completion target: March 2018



FAIRFIELD CAMPUS ENTRY SIDEWALK



- Construction in progress
- On-campus sidewalk poured and light poles installed
- Delayed due to weather and other requirements
- Completion target March 2018



FAIRFIELD CAMPUS DIRECTORIES



- Completed installation of 4 directory map signs

VACAVILLE CENTER INTERSECTION IMPROVEMENTS PROJECT



- Construction nearly completed
- Must wait for continuous dry and warm weather to complete asphalt slurry and road striping
- Completion target April 2018



VACAVILLE CLASSROOM BUILDING (ANNEX)



- Contract awarded in December
- Demo and construction in progress
- Completion target: July 2018
- Occupancy: Fall semester



VACAVILLE CENTER HVAC UPGRADE



- Plans approved by DSA
- Issued for bid in January
- Construction summer 2018



QUESTIONS?

