

**MEASURE Q PROGRESS
UPDATE REPORT
JANUARY – MARCH 2018**

MAY 16, 2018

PROGRAM OVERVIEW

- \$5.8M expended this quarter; \$127M expended to date
- Series A funds spent out
- Revisions to District Standards and FF&E Guidelines approved
- Report on Two-Year Pilot Small, Local and Diverse Business Program
- FY 2016-2017 Financial & Performance Audit approved by Board
- Citizens Bond Oversight Committee:
 - Board appointed new CBOC members
 - CBOC completed FY 2015-2016 Annual Report
 - CBOC completed FY 2016-2017 Annual Report April 3



SCIENCE BUILDING - PHASE 1



- Foundation and underslab utilities completed
- Floor slab poured
- Concrete tilt up walls to be poured in April
- Exterior tilt-up walls to be stood in place May 23-24
- Substantial Completion January 2019



PROPOSED MAIN ENTRY SIGNAGE



LIBRARY/LEARNING RESOURCE CENTER



- CEQA ISMND completed and approved by Board
- Schematic Design completed
- 50% Design Development submittal in April
- Submitted Preliminary Plans to Chancellor's Office for Working Drawing phase funding release



HORTICULTURE RESTROOM BUILDING



- Sitework contract awarded
- Sitework and foundation started in April
- Modular restroom building fabrication in progress
- Completion target: June 2018



FAIRFIELD CAMPUS ENTRY SIDEWALK



- Concrete sidewalk completed
- Landscaping completed
- City light pole installed
- Paving striping completed
- Completed April

SOFTBALL BLEACHER PATH OF TRAVEL



- Constructed new ADA compliant sidewalk from softball field to restroom building near tennis courts
- Completed April



FAIRFIELD INFRASTRUCTURE PROJECTS



SUB-STATION REPLACEMENT

- Sidewalk infill completed
- Utility trench patch completed
- Fence enclosure in April

B-100 DATA CENTER GENERATOR

- Underground utility work completed
- Concrete pad & fence posts installed
- Equipment being fabricated
- Equipment install target: May 26




GAS LINE REPLACEMENT

- In progress - 45% complete

VACAVILLE CLASSROOM BUILDING (ANNEX)



- Construction in progress
- New roof trusses installed
- Old concrete roof tiles removed
- ADA ramp improvements in progress
- Completion target: July 2018

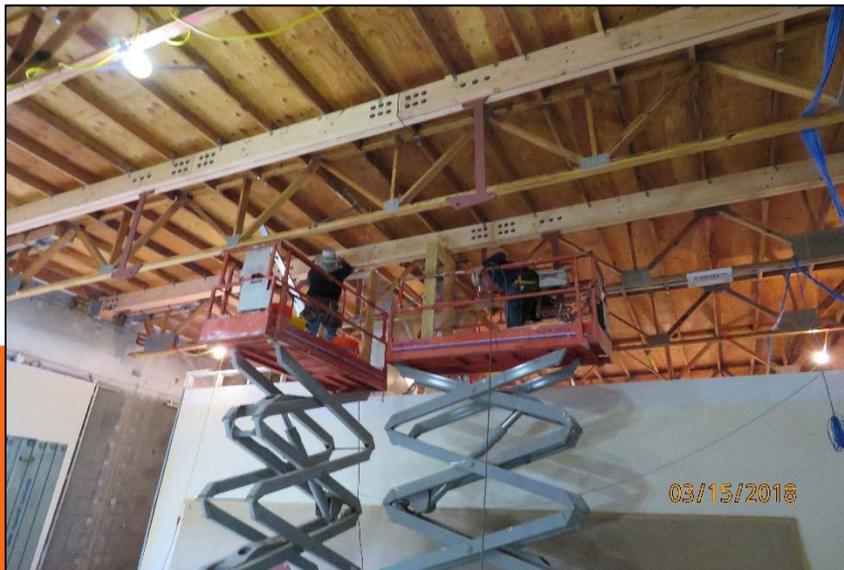

VACAVILLE CENTER HVAC UPGRADE



- Construction contract awarded
- Construction summer 2018



VACAVILLE CENTER INTERSECTION IMPROVEMENTS PROJECT



- Construction nearly completed
- Must wait for continuous dry and warm weather to complete asphalt slurry and road striping
- Completion target April 2018



QUESTIONS?

