

# MEASURE Q ACTIVITY JULY – SEPTEMBER 2018

---

- Program Overview:

- \$8,513,994 expended this quarter
- Total expended \$144,506,105 to date or 41.5% of total \$348M

# MEASURE Q QUARTERLY PROJECT STATUS UPDATE SUMMARY

---

## • Projects In Progress

- Library/Student Learning Center
- Science Building/Veteran's Affairs
- Information Technology Upgrades
- Horticulture Restroom
- Sign Projects for I200 and Aeronautics Buildings

## • Projects Completed

- Vacaville Annex Code Compliance
- Vacaville Intersection Upgrade
- Vacaville HVAC Project
- Building I800 Exiting Corridor
- Building I800 Maker's Space & Robotics

# SCIENCE BUILDING & VETERANS CENTER

---

- Interior wall framing complete
- Sheetrock is 95%
- Exterior Doors hung, interior frames are hung
- Solar panels installed on roof
- Mechanical, Electrical, Plumbing 95% rough in complete
- Exterior site work underway,
  - Student Plaza
  - Seat Wall
  - Sidewalk
  - Fire road
- Occupancy Summer 2019



# LIBRARY/LEARNING RESOURCE CENTER

---




- Field survey for underground utilities verification completed
- Furniture and Equipment Inventory of Existing Library Completed (determine reuse potentials)
- Conduct Hazardous Materials Survey of Existing Library (required for demolition)
- 75% Construction Documents (CDs) Complete
- Third DSA Collaborative Meeting held

# HORTICULTURE RESTROOM BUILDING

---

- Foundation Poured
- Modular building in fabrication
- Building scheduled to be delivered and installed starting November 1<sup>st</sup>.

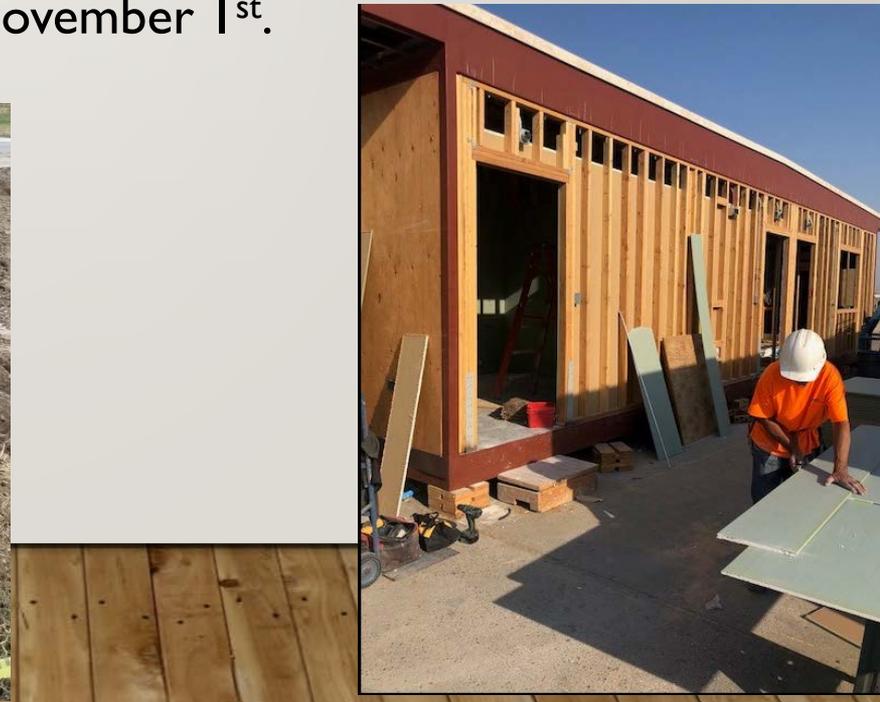

# VACAVILLE CENTER INTERSECTION IMPROVEMENTS PROJECT

- Completion SEPTEMBER 2018





I'm Finished!!!



[www.txt2pic.com](http://www.txt2pic.com)

# VACAVILLE CENTER HVAC UPGRADE PROJECT

---

- Project Complete



# VACAVILLE CLASSROOM BUILDING (ANNEX)



# QUESTIONS?

---

